



গণপ্রজাতন্ত্রী বাংলাদেশ সরকার  
শ্রম ও কর্মসংস্থান মন্ত্রণালয়  
কলকারখানা ও প্রতিষ্ঠান পরিদর্শন অধিদপ্তর

"শ্রমজীবী মানুষের অধিকার,  
বৈষম্যহীন বাংলাদেশের অঙ্গীকার"

ক্যাপ পর্যবেক্ষণের তথ্য


কারখানার নাম	কালার স্টিচ লিঃ
ঠিকানা	119, Ashkona Medical Road,
কারখানার কোড	DHK132
কালার কোড	
মূল্যায়নের ধরণ: <a href="#">কঠামোগত মূল্যায়ন</a>	পর্যবেক্ষণের তারিখ: ০২-০৪-২০২৩
১. পর্যবেক্ষণ	

পরিদর্শন পর্যবেক্ষণ	Moderately stressed column
কাপ আইটেম ক্যাটাগরি	

#### ১.১. কার্যক্রম

কার্যক্রম	Prepared the details As-built Architectural and structural drawings.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not taken any action but agreed to complete the issue within the given timeline.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	০১-০১-১৯৭০
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	Previous Timeline: N/A. they have no CAP-01 report. Final Timeline: 4/12/2017. Factory has no taken any action yet but they will have agreed to complete within timeline. 28.01.2020: They Submitted as built structural, Architectural drawing, floor load plan, DEA report and CD dated 27.12.18. and 04.11.19 dated in task force meeting has decided retro-fitting drawing should submit within one month. retro-fitting drawing has not submitted yet. 08/10/2020: Same as previous status. Due to corona virus pandemic the remediation work has been delayed. 26.01.2021: Correction Review design or drawing has not submitted yet. 10/06/2021: The factory has prepared its As-built drawings and submitted to DIFE but there is no site copy is found during the visit. 07/08/2022: DEA report must be resubmitted to DIFE as soon as possible. 02/04/2023: Factory was closed during on visit day. All floors are locked but Another factory "Euroasia Knitwear Ltd." found on 3rd & 4th floor of the building.

#### সংযুক্তিসমূহ (৪)

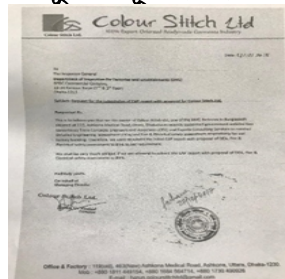

#### ২. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Moderately stressed column
কাপ আইটেম ক্যাটাগরি	

### ২.১. কার্যক্রম

কার্যক্রম	Verify insitu concrete stresses either by 4 Nos. 100mm dia. Cores test or existing cylinder strength data for the identified the stresses of the columns. Also conduct the ferro scan report for chacking the rebars of the columns, beams & slabs
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not taken any action but agreed to complete the issue within the given timeline.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	০১-০১-১৯৭০
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	Previous Timeline: N/A. they have no CAP-01 report. Final Timeline: 4/12/2017. Factory has no taken any action yet but they will have agreed to complete within timeline. 28.01.2020: Consulting firm taking core cutting sample and all necessary test report submitted to DIFE. 08/10/2020: Same as previous status. Due to corona virus pandemic the remediation work has been delayed. 26.01.2021: Correction Review design or drawing has not submitted yet. 10/06/2021: This issues are covered in DEA report and submitted to DIFE but there is no site copy is found during the visit. The factory has not been submitted its revised documents to DIFE according to the Taskforce review yet. 07/08/2022: DEA report must be resubmitted to DIFE as soon as possible. 02/04/2023: Factory was closed during on visit day. All floors are locked but Another factory "Euroasia Knitwear Ltd." found on 3rd & 4th floor of the building.

### সংযুক্তিসমূহ (২)



### ৩. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Moderately stressed column
কাপ আইটেম কাটাগরি	

### ৩.১. কার্যক্রম

কার্যক্রম	Take Structural analysis to ascertain the safety of the structure and recommending remediation measures if required. Also vertical extension above the roof, beyond approval may be allowed if detail assesment of the structures ( DEA ). Produce and actively manage a loading plan for all floor plates within the factory giving consideration to floor capacity and column capacity.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not taken any action but agreed to complete the issue within the given timeline.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	০১-০১-১৯৭০
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	Previous Timeline: N/A. they have no CAP-01 report. Final Timeline: 4/12/2017. Factory has no taken any action yet but they will have agreed to complete within timeline. 28.01.2020: Vertical extension above the roof, which is use for Dinning. This report also included in DEA report. Which is submitted to DIFE. 04.11.19 dated in task force meeting has decided retrofitting drawing should submit within one month. retrofitting drawing has not submitted yet. 08/10/2020: Same as previous status. Due to corona virus pandemic the remediation work has been delayed. 26.01.2021: Correction Review design or drawing has not submitted yet. 10/06/2021: This issues are covered in DEA report and submitted to DIFE. But the factory has not been submitted its revised documents to DIFE according to the Taskforce review yet. 07/08/2022: DEA report must be resubmitted to DIFE as soon as possible. 02/04/2023: Factory was closed during on visit day. All floors are locked but Another factory "Euroasia Knitwear Ltd." found on 3rd & 4th floor of the building.

### সংযুক্তিসমূহ ( ৪ )

