



গণপ্রজাতন্ত্রী বাংলাদেশ সরকার  
শ্রম ও কর্মসংস্থান মন্ত্রণালয়  
কলকারখানা ও প্রতিষ্ঠান পরিদর্শন অধিদপ্তর

"শ্রমজীবী মানুষের অধিকার,  
বৈষম্যহীন বাংলাদেশের অঙ্গীকার"

ক্যাপ পর্যবেক্ষণের তথ্য


কারখানার নাম	কোর এইচ ডাইং এন্ড প্রিন্টিং লিঃ
ঠিকানা	Arakan Road, Word No: 06, Kalarpool Chapra, Patia, Chattogram
কারখানার কোড	CHT072
কালার কোড	
মূল্যায়নের ধরন: <a href="#">অগ্নি মূল্যায়ন</a>	পর্যবেক্ষণের তারিখ: <a href="#">২৫-০৫-২০২২</a>
১. পর্যবেক্ষণ	

পরিদর্শন পর্যবেক্ষণ	Location-1st to 5th floor of B & C Building, Dyeing Shed & Printing Shed The maximum travel distance from any location of the floor to the nearest emergency exit was 76 m, 60 m, 51 meter at 1st to 5th floor of B & C Building, Dyeing Shed & Printing Shed respectively , which was not fulfilled the requirement of RMG guideline.
কাপ আইটেম কাটাগরি	

#### ১.১. কার্যক্রম

কার্যক্রম	Within 6 Weeks, Prepare proper plan and design for one or more exit with stair in a way not to exceed the maximum travel distance ( 45 meter ) of building B &C, & one or more exit for shed to meet the minimum travelway. or If the factory design to equip with an automated fire alarm, portable fire-fighting system and appropriate standpipe and hose system through the entire building the length of travel should not be exceed 60 meter.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	চলমান
মন্তব্য	The factory design to equip with an automated fire alarm, portable fire-fighting system and appropriate standpipe and hose system through the entire building and the length of travel was below 60 meter and factory will submitted the document to DIFE for approval and it is under review.17/08/2020 :Approval has not been given yet . 02-11-2020:Approval has not been given yet .On 17.01.2021:Factory submitted fire design drawing on dated 11.09.2019 at dife.They got correction of design drawing from taskforce but consultancy firm doesnt submitted yet. "25-05-22 (CCVV): The factory has submitted Fire Hydrant System, Detection system and Separation drawing on 11.09,2019 to DIFE for approval. During visit, no drawing found to verify travel distance."

#### সংযুক্তিসমূহ (১)

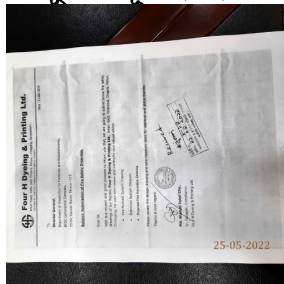


#### ২. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-1st to 5th floor of B & C Building, Dyeing Shed & Printing Shed The maximum travel distance from any location of the floor to the nearest emergency exit was 76 m, 60 m, 51 meter at 1st to 5th floor of B & C Building, Dyeing Shed & Printing Shed respectively , which was not fulfilled the requirement of RMG guideline.
ক্যাপ আইটেম ক্যাটাগরি	

## ২.১. কার্যক্রম

কার্যক্রম	Within 6 Months, Implement the plan and design for one or more exit with staircase in building B & C and Implement one or more exit in sheds. or Implement automated fire alarm, portable fire-fighting system and appropriate standpipe and hose system through the entire building.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	১৬-০২-২০২৩
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Implemented automated fire alarm, portable fire-fighting system and appropriate standpipe and hose system through the entire building.17/08/2020 :They installed automated fire alarm, portable fire-fighting system and appropriate standpipe and hose system through the entire building but till now design drawing is reviewing at taskforce. 02-11-2020:They installed automated fire alarm, portable fire-fighting system and appropriate standpipe and hose system through the entire building but till now design drawing is reviewing at taskforce.On 17.01.2021:Fire detection system & hydrent system installation is ongoing without design approval of dife. "25-05-22 (CCVV) : The factory has submitted Fire Hydrant System, Detection system and Separation drawing on 11.09,2019 to DIFE for approval. During visit, no drawing found to verify travel distance."

## সংযুক্তিসমূহ (১)




## ৩. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-All exit doors at egress route ( Building and Shed ) All exit doors were provided with steel sliding, collapsible security gate & wooden type doors installed at egress route and do not open in the direction of the travel.
ক্যাপ আইটেম ক্যাটাগরি	

### ৩.১. কার্যক্রম

কার্যক্রম	Replace all existing exit doors on evacuation routes at building and sheds, exit doors with side hinged type door, which swing outward and in the direction of travel. Swinging of the door should not constrict the width of the corridor / passage below 0.9 meter.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Factory provided outward sewing door at egress route in all exit way. On 17-02-20: they replaces all existing exit door. 17-08-20: They installed fire door. 02-11-2020: They installed fire door. On 17.01.2021: fire door was provided in all building exit but shed door is sliding door which is risky & not applicable. 25-05-22 (CCVV): During visit, all the doors have been found side swinging outward opening including shed's door but no design drawing found regarding this matter to verify.

### সংযুক্তিসমূহ (১)




### ৪. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-All exit doors at egress route All floors exit doors were provided with steel sliding, collapsible security gate & wooden type doors installed with locking arrangement at egress route and there was a chance that doors get locked due to any obstruction in opening/closing.
ক্যাপ আইটেম ক্যাটাগরি	

#### ৪.১. কার্যক্রম

কার্যক্রম	Remove all locking device from all egress door. All exit doors should be open-able from the side they serve without the use of a key.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Factory provided outward sewing door at egress route in all exit way and without locking device. On 17-02-20: They remove all locking device from all egress door..17-08-20: All locking devices have been removed. 02-11-2020: All locking devices have been removed. On 17.01.2021: fire door was provided in all building exit but shed door is sliding door which is risky & not applicable. 25-05-22 (CCVV): During visit, all the doors have been found side swinging outward opening including shed's door but no design drawing found regarding this matter to verify.

#### সংযুক্তিসমূহ (২)

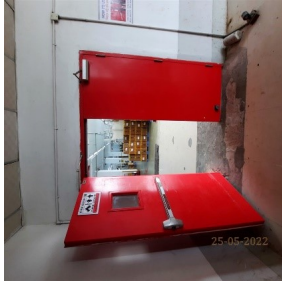

#### ৫. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location- All Stairways of 6 storey Building No door, collapsible security gate, wooden & glass type doors were found at the staircase of the factory building, which were not self-closing type at evacuation route, so stairs required fire rated self-closing doors. At the audit date, few of the fire door was purchased already and within 2-3 months factory will implemented fire door at the staircase.
ক্যাপ আইটেম ক্যাটাগরি	

#### ৫.১. কার্যক্রম

কার্যক্রম	Doors in stair should be outward opening, side-swing, self closing, non-lockable 1.5 hours fire rated doors and 2 hour fire rated wall in all stair way to enclose at 6 storied building B & C.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	1.5 hours fire rated doors and 2 hour fire rated wall was provided at all stair way of building B & C. 17-08-20: The Stair way is protected by fire door and 2 hour fire rated wall. 02-11-2020: The Stair way is protected by fire door and 2 hour fire rated wall..On 17.01.2021:Fire door has been installed in all rcc building.


#### ৬. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-1st to 5th floor of B & C building At 1st to 5th floor of B & C building, large storage area was found without fire separation adjacent to the knitting section and the stair.
ক্যাপ আইটেম ক্যাটাগরি	

#### ৬.১. কার্যক্রম

কার্যক্রম	Within 6 Weeks, Prepare proper plan and design for 2 hrs fire rated barrier with 1.5 hrs fire rated door for storage area at B & C building, 1st to 5th floor.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not taken any action but agreed to complete the issue within the given timeline.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	০৯-০৯-১৯৭০
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	চলমান
মন্তব্য	Previous timeline : NA, during CAP explanation (CAP01) factory claimed completed Final Timeline: 23/08/2017 Not taken any action regarding this issue but factory agreed to complete the issue within timeline. On 17-02-20: The factory submitted design and drawing at DIFE. 02-11-2020: Design and Drawing has been submitted but not approved yet. On 17.01.2021: Factory submitted fire design drawing on dated 11.09.2019 at dife. They got correction of design drawing from taskforce but consultancy firm doesnt submitted yet. "25-05-22 (CCVV): The factory has submitted Fire Hydrant System, Detection system and Separation drawing on 11.09,2019 to DIFE for approval. "

#### সংযুক্তিসমূহ (১)

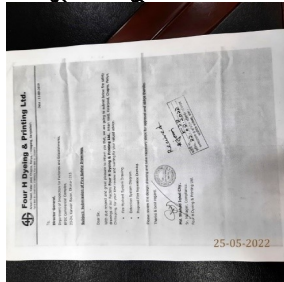




#### ৭. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-1st to 5th floor of B & C building At 1st to 5th floor of B & C building, large storage area was found without fire separation adjacent to the knitting section and the stair.
ক্যাপ আইটেম ক্যাটাগরি	

#### ৭.১. কার্যক্রম

কার্যক্রম	Within 6 Months, Provide 2 hrs fire rated barrier with 1.5 hrs fire rated door for storage area of mentioned location.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	১৬-০২-২০২৩
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Provided 2 hrs fire rated barrier with 1.5 hrs fire rated door for storage area of mentioned location. On 17-02-20: They provided fire rated barrier with 1.5 hrs fire rated door but their design drawing still didn't get approval from DIFE. 02-11-2020:They provided fire rated barrier with 1.5 hrs fire rated door but their design drawing still didn't get approval from DIFE.On 17.01.2021:Factory submitted fire design drawing on dated 11.09.2019 at dife.They got correction of design drawing from taskforce but consultancy firm doesnt submitted yet.Fire door & fire rated barrier has been given in storage area. "25-05-22 (CCVV) : At 1st to 5th floor of B & C building, there have some large storage area without fire separation adjacent to the knitting section and some area found free from storage during visit."

#### সংযুক্তিসমূহ ( ৪ )

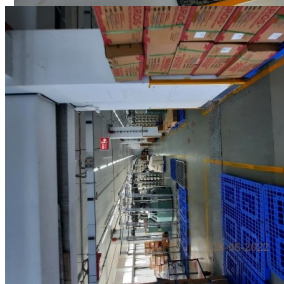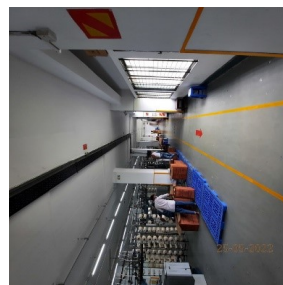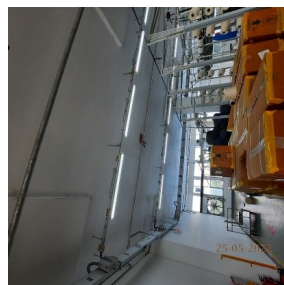


পরিদর্শন পর্যবেক্ষণ	Location-Chemical Store at Industrial Shed-4 Chemical store was located at Industrial shed-4 adjacent to maintenance section & leftover storage without fire rated construction.
ক্যাপ আইটেম ক্যাটাগরি	

#### ৮.১. কার্যক্রম

কার্যক্রম	Within 6 Weeks, Prepare proper plan and design for 4 hours fire rated barriers with 2 hours fire rated door at chemical store, which located at the adjacent to maintenance section & leftover storage at Industrial shed-4.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not taken any action but agreed to complete the issue within the given timeline.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	০১-০১-১৯৭০
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Previous timeline : NA, during CAP explanation (CAP01) factory claimed completed Final Timeline: 23/08/2017 Not taken any action regarding this issue but factory agreed to complete the issue within timeline.17-08-20: design and Drawing has been submitted but not approved yet. 02-11-2020: Design and Drawing has been submitted but not approved yet. 25-05-22 (CCVV) : The factory has submitted Fire Hydrant System, Detection system and Separation drawing on 11.09,2019 to DIFE for approval.

#### সংযুক্তিসমূহ (১)

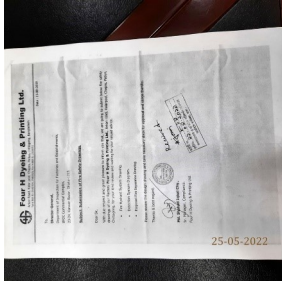


#### ৯. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-Chemical Store at Industrial Shed-4 Chemical store was located at Industrial shed-4 adjacent to maintenance section & leftover storage without fire rated construction.
ক্যাপ আইটেম ক্যাটাগরি	

#### ৯.১. কার্যক্রম

কার্যক্রম	Within 6 months, Provide 4 hours fire rated barriers with 2 hours fire rated door at chemical store, which located at the adjacent to maintenance section & leftover storage.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not taken any action but agreed to complete the issue within the given timeline.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	০১-০১-১৯৭০
সংশোধিত সময়সীমা	১৬-০২-২০২৩
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Previous timeline : NA, during CAP explanation (CAP01) factory claimed completed Final Timeline: 23/11/2017 Not taken any action regarding this issue but factory agreed to complete the issue within timeline. On 17-02-20: They provided fire rated barrier with 2 hrs fire rated door but their design drawing still didn't get approval from DIFE. 17/08/2020: They provided fire rated barrier with 2 hrs fire rated door but their design drawing still didn't get approval from DIFE. 02-11-2020: They provided fire rated barrier with 2 hrs fire rated door but their design drawing still didn't get approval from DIFE. On 17.01.2021: Factory submitted fire design drawing on dated 11.09.2019 at dife. They got correction of design drawing from taskforce but consultancy firm doesn't submitted yet. Fire door & fire rated barrier has been given in storage area. 25-05-22 (CCVV): Chemical store is now located at ground floor of building-1 and found properly fire separated from the others occupancy. But no design drawing found regarding this matter to verify.

#### সংযুক্তিসমূহ (৩)

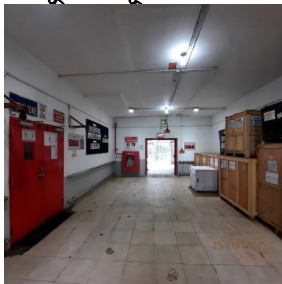


#### ১০. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-Ground floor of B & C building & ground floor of dyeing & printing shed Emergency lighting was provided but not sufficient at all evacuation pathways of working floors.
ক্যাপ আইটেম ক্যাটাগরি	

#### ১০.১. কার্যক্রম

কার্যক্রম	The egress paths should be illuminated with emergency lighting with power back-up supply & illumination should be a minimum of 10 lux for all corridors & exit doors. Aisles should be provided with a minimum 2 lux.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not taken any action but agreed to complete the issue within the given timeline.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	০১-০১-১৯৭০
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Previous timeline : NA, during CAP explanation (CAP01) factory claimed completed Final Timeline: 23/08/2017 Not taken any action regarding this issue but factory agreed to complete the issue within timeline. On 17-02-20: They provide emergency lighting with emergency power back up . 02-11-2020: They provide emergency lighting with emergency power back up . On 17.01.2021: emergency lighting with emergency power back up has been given moderately but all aisle isn't covered. 25-05-22 (CCVV) : Emergency lighting has been provided but not sufficient at all evacuation pathways of working floors.

#### সংযুক্তিসমূহ (৩)

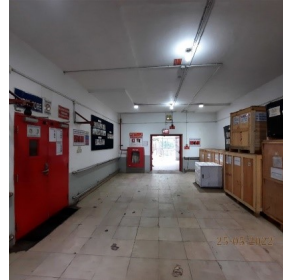


#### ১১. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	The factory has not implemented automatic detection system, only stand alone type smoke detector system implemented. Smoke alarm activation sound only a local alarm and doesn't provide automatic fire alarm notification of occupants. At the time of audit, factory has confirmed automatic detection and alarm system drawing and will implemented automatic detection and alarm system within 2-3 months.
ক্যাপ আইটেম ক্যাটাগরি	

#### ১১.১. কার্যক্রম

কার্যক্রম	Within 6 weeks, Produce design and plan for automatic detection system with automatic fire alarm at all floor of building and sheds.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	চলমান
মন্তব্য	Produced design and plan for automatic detection system with automatic fire alarm at all floor of building and sheds and factory will submitted the document to DIFE and it is under review. 17-08-20: design and Drawing has been submitted but not approved yet. 02-11-2020: Design and Drawing has been submitted but not approved yet. On 17.01.2021: Factory submitted fire design drawing on dated 11.09.2019 at dife. They got correction of design drawing from taskforce but consultancy firm doesnt submitted yet. 25-05-22 (CCVV): The factory has submitted Fire Hydrant System, Detection system and Separation drawing on 11.09,2019 to DIFE for approval.

#### সংযুক্তিসমূহ (১)



#### ১২. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	The factory has not implemented automatic detection system, only stand alone type smoke detector system implemented. Smoke alarm activation sound only a local alarm and doesn't provide automatic fire alarm notification of occupants. At the time of audit, factory has confirmed automatic detection and alarm system drawing and will implemented automatic detection and alarm system within 2-3 months.
ক্যাপ আইটেম ক্যাটাগরি	

#### ১২.১. কার্যক্রম

কার্যক্রম	Within 6 months, Install automatic detection system with automatic fire alarm at all floors of buildings and sheds.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	১৬-০২-২০২৩
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Installed automatic detection system with automatic fire alarm at all floors of buildings and sheds. But their design drawing still didn't get approval from DIFE. 17/08/20: same as before. 02-11-2020: Installed automatic detection system with automatic fire alarm at all floors of buildings and sheds. But their design drawing still didn't get approval from DIFE. On 17.01.2021: Fire detection system has been installed in all rcc building but all shed isn't cover up for fire detection system as well as their design drawing not approved yet. 25-05-22 (CCVV): Automatic detection and alarm system installation process is on-going at all floors of buildings and sheds. Final T & C is yet not done.

#### সংযুক্তিসমূহ (২)



#### ১৩. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-All Floor of B & C Building & All Shed The quantities of detector was not adequate at all floor of B & C building & all shed of the factory. At the audit date, factory confirmed automatic detection and alarm system drawing and will implemented automatic detection and alarm system within 2-3 months.
ক্যাপ আইটেম ক্যাটাগরি	

#### ১৩.১. কার্যক্রম

কার্যক্রম	Provide adequate nos. of automatic smoke detectors with alarm system to cover the entire factory buildings and sheds.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Provided adequate nos. of automatic smoke detectors with alarm system to cover the entire factory buildings and sheds. 02-11-2020: Provided adequate nos. of automatic smoke detectors with alarm system to cover the entire factory buildings and sheds. On 17.01.2021: Fire detection system has been installed in all rcc building but all shed isnt coverup for fire detection system as well as their design drawing not approved yet. 25-05-22 (CCVV) : Automatic detection and alarm system installation process is on-going at all floors of buildings and sheds.

#### সংযুক্তিসমূহ (২)




#### ১৪. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	No dedicated fire pump or hydrant system was available for fire fighting. At the audit date, factory confirmed hydrant system drawing and will implemented hydrant system within 2-3 months.
ক্যাপ আইটেম ক্যাটাগরি	

#### ১৪.১. কার্যক্রম

কার্যক্রম	Within 6 Weeks, Prepare proper design and plan for dedicated fire pump with alternate backup power supply.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	চলমান
মন্তব্য	Prepared proper design and plan for dedicated fire pump with alternate backup power supply and factory will submitted the document to DIFE and it is under review. 17-08-20: design and Drawing has been submitted but not approved yet. 02-11-2020: Design and Drawing has been submitted but not approved yet. On 17.01.2021: Factory submitted fire design drawing on dated 11.09.2019 at dife. They got correction of design drawing from taskforce but consultancy firm doesnt submitted yet. 25-05-22 (CCVV): The factory has submitted Fire Hydrant System, Detection system and Separation drawing on 11.09,2019 to DIFE for approval.

#### সংযুক্তিসমূহ (১)

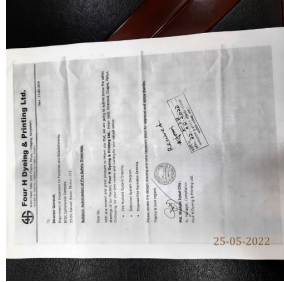



#### ১৫. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	No dedicated fire pump or hydrant system was available for fire fighting. At the audit date, factory confirmed hydrant system drawing and will implemented hydrant system within 2-3 months.
ক্যাপ আইটেম ক্যাটাগরি	

#### ১৫.১. কার্যক্রম

কার্যক্রম	Within 6 months, Install dedicated fire pump with alternate backup power supply.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	১৬-০২-২০২৩
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Installed dedicated fire pump with alternate backup power supply.but design drawing didn't get approval yet. 02-11-2020:Installed dedicated fire pump with alternate backup power supply.but design drawing didn't get approval yet.On 17.01.2021:Factory submitted fire design drawing on dated 11.09.2019 at dife.They got correction of design drawing from taskforce but consultancy firm doesnt submitted yet.Hydrant system installed without approval of design drawing. 25-05-22 (CCVV) : Dedicated fire pump and fire hydrant system already installed but final T&C is not yet done.

#### সংযুক্তিসমূহ (৩)

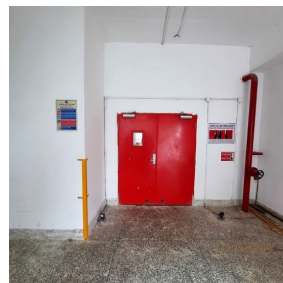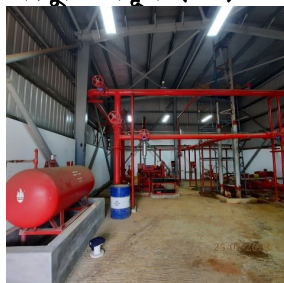


#### ১৬. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-All Floor of B & C Building & All Shed Diameter of standpipe was fulfilled however the diameter of hose pipe was 1.0 inch, which was not fulfilled the requirement of code.
ক্যাপ আইটেম ক্যাটাগরি	

#### ১৬.১. কার্যক্রম

কার্যক্রম	Replace existing 1 inch hose pipe with 1.5 inch hose pipe to meet the requirement of RMG guideline.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ সপ্তাহ
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	২৭-০৯-২০২২
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	Provided 1.5 inch hose pipe for the whole factory building.17/08/20:diameter of hose pipe is 1.5 inch. 02-11-2020:Provided 1.5 inch hose pipe for the whole factory building.On 17.01.2021: They Provided 1.5 inch hose pipe but design drawing doesnt approve yet. 25-05-22 (CCVV): The factory has submitted Fire Hydrant System, Detection system and Separation drawing on 11.09,2019 to DIFE for approval.

#### সংযুক্তিসমূহ (১)

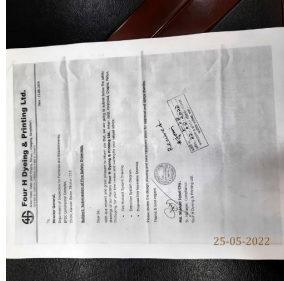

#### ১৭. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Location-5th Floor of B & C Building The performance of hose ( water pressure ) was not satisfactory. The water throw of jet was around 10 ft. distance.
কাপ আইটেম ক্যাটাগরি	

#### ১৭.১. কার্যক্রম

কার্যক্রম	Stand pipe supplying first aid hose should have minimum pressure of 200 KPa.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have completed this issue.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	১৬-০২-২০২৩
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	The performance of hose ( water pressure ) was not satisfactory. 17/08/20:Due to heavy rainfall can't check the pressure. 02-11-2020:The performance of hose ( water pressure ) was not satisfactory.On 17.01.2021: hose pipe pressure was lower than standard.The water throw of jet was around 10-15 ft. distance. 25-05-22 ( CCVV ) : Fire hydrant system already installed but final T&C is not yet done.

#### সংযুক্তিসমূহ (১)

