



গণপ্রজাতন্ত্রী বাংলাদেশ সরকার
শ্রম ও কর্মসংস্থান মন্ত্রণালয়
কলকারখানা ও প্রতিষ্ঠান পরিদর্শন অধিদপ্তর

"সুস্থ শ্রমিক, শোভন কর্মপরিবেশ;
গড়ে তুলবে স্মার্ট বাংলাদেশ"

ক্যাপ পর্যবেক্ষণের তথ্য


কারখানার নাম	এ আর আর ডিসেমোটিক্স
ঠিকানা	3, NO, MADRASA BAZAR ROAD, MATUAIL, JATRABARI, DEMRA, DHAKA
কারখানার কোড	DHK007
কালার কোড	
মূল্যায়নের ধরণ: কাঠামোগত মূল্যায়ন	পর্যবেক্ষণের তারিখ: ০৫-০৪-২০২৩
১. পর্যবেক্ষণ	

পরিদর্শন পর্যবেক্ষণ	Floor Load Plan
ক্যাপ আইটেম ক্যাটাগরি	

১.১. কার্যক্রম

কার্যক্রম	The factory owner has been instructed to prepare and submit a load plan for vetting. Once it is submitted by the factory owner, it will be duly vetted.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We will not take any action yet but we will complete this issues within this time line.
অগ্রাধিকার	প্রযোজ্য নয়
চূড়ান্ত সমস্বসীমা	০১-০১-১৯৭০
সংশোধিত সমস্বসীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	02/07/2020: As per 49th Taskforce meeting on 10/10/2018, the factory management were told to re-submit structural design & drawings with Dynamic Analysis within one month. The factory management re-submit structural design & drawings to DIFE but not with Dynamic Analysis. Now the factory management is told to submit all structural design & drawings along with DEA & retrofit drawings by Dynamic Analysis within 31/07/2020. The factory management have removed their non-structural roof top shed as per last visit concern. 19/10/2020: The factory is advised to re-submit its corrected structural design and drawings within the timeline 19-November, 2020 by an internal meeting with the consultancy firm of factory and RCC engineers. Now they are preparing to re-submit their structural design and drawings. 06/01/2021: This issue has covered with DEA. Factory has not re-submitted review design drawing yet. Consulting firm has worked on it. 06/05/2021: Factory management already submitted their design drawing, DEA to DIFE for approval on 30.05.2019 but there are some corrections and they are fail to submit on time. 22.08.2021: Factory management already submitted their design drawing, DEA to DIFE for approval on 30.05.2019 but there are some corrections and they are fail to submit on time. No action has been taken yet. 04/08/2022: DEA report and floor load plan to be resubmitted to DIFE as soon as possible. 05/04/2023: DEA report and floor load plan to be resubmitted to DIFE.

সংযুক্তিসমূহ (৪)

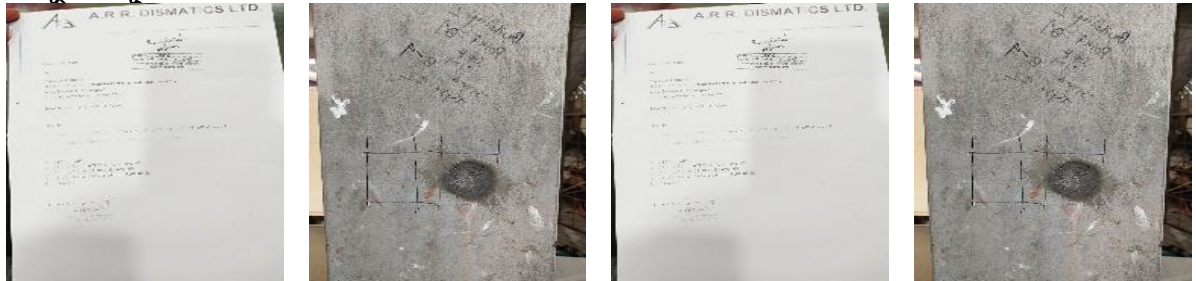

২. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Vertical & Horizontal Extension
কাপ আইটেম ক্যাটাগরি	

২.১. কার্যক্রম

কার্যক্রম	No horizontal or vertical extension of the building shall be made without detail engineering assessment.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We will not take any action yet but we will complete this issues within this time line.
অগ্রাধিকার	প্রযোজ্য নয়
চূড়ান্ত সময়সীমা	০১-০১-১৯৭০
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	02/07/2020: No vertical or horizontal extension found on the visiting date. 19/10/2020: During the visit, no vertical or horizontal extension is observed. 06/01/2021: No vertical & Horizontal extension during inspection. 06/05/2021: There was no horizontal and vertical extension found on the date of inspection. 22.08.2021: There was no horizontal and vertical extension found on the date of inspection. 04/08/2022: No horizontal or vertical extension was found during the inspection date. 05-04-2023: Completed.

সংযুক্তিসমূহ (২)

