



গণপ্রজাতন্ত্রী বাংলাদেশ সরকার  
শ্রম ও কর্মসংস্থান মন্ত্রণালয়  
কলকারখানা ও প্রতিষ্ঠান পরিদর্শন অধিদপ্তর

"সুস্থ শ্রমিক, শোভন কর্মপরিবেশ;  
গড়ে তুলবে স্মার্ট বাংলাদেশ"

ক্যাপ পর্যবেক্ষণের তথ্য


কারখানার নাম	আলীম নীট ওয়ারস লিঃ
ঠিকানা	27, Harunabad, Senanibas Road, Section # 12, Pallabi, Dhaka
কারখানার কোড	DHK037
কালার কোড	
মূল্যায়নের ধরণ: <a href="#">কাঠামোগত মূল্যায়ন</a>	পর্যবেক্ষণের তারিখ: ০২-০৪-২০২৩
১. পর্যবেক্ষণ	

পরিদর্শন পর্যবেক্ষণ	Detailed Engineering Assessment
ক্যাপ আইটেম ক্যাটাগরি	

### ১.১. কার্যক্রম

কার্যক্রম	A detailed Engineering assessment should be completed
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not been taken any action yet but agreed to complete within the given timeline.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	১১-০৮-২০১৭
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	<p>Previous Timeline: N/A, during CAP (CAP-01) explanation factory claimed completed. Final Timeline: 08/11/2017. Not taken any action regarding this issue but factory agreed to complete the issue within the timeline. 09/03/2020: DEA has been submitted to DIFE for approval. 02/09/2020: DEA has been submitted on 04/07/19 for approval but not approved yet by taskforce. 08/12/2020: DEA has been submitted to DIFE on 04.07.19 for approval. 17/02/2021: A notification meeting held on September 23, 2020 and some review was found But review item is not submitted yet. 09/06/2021: The factory management have submitted all structural design &amp; drawings by an enlisted firm of DIFE to DIFE RCC on 04/07/2019. A notification meeting held on RCC office regarding this issue in presence of the factory management &amp; consulting firm personnel on 23/07/2020. They were told to re-submit these design &amp; drawings with some reviews to DIFE RCC within 11/10/2020. But those are not submitted yet. Now the factory management is instructed to submit these design &amp; drawings with proper corrections by their consulting firm to DIFE RCC within 10/07/2021. 23.08.2021: Correction Design drawing not submitted yet. Now the factory management is instructed to submit these design &amp; drawings with proper corrections by their consulting firm to DIFE RCC 16/08/2022: DEA report must be resubmitted to DIFE for approval as soon as possible. 02/04/2023: DEA report should be resubmitted to DIFE for approval as soon as possible.</p>

### সংযুক্তিসমূহ ( ৪ )

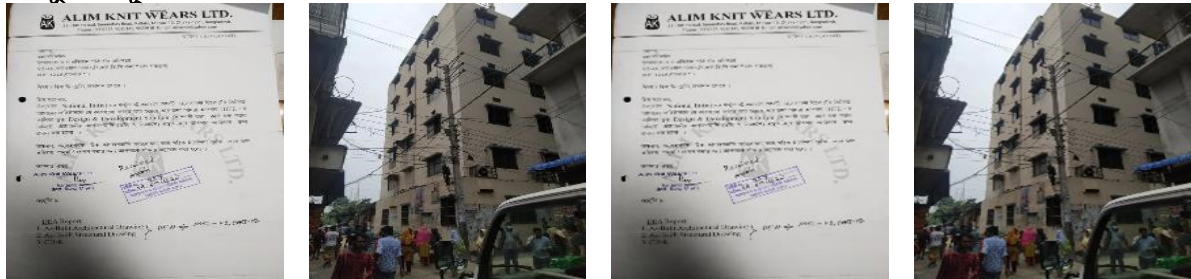





### ২. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	As built drawing
কাপ আইটেম ক্যাটাগরি	

### ২.১. কার্যক্রম

কার্যক্রম	A as built drawing needs to prepare
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not been taken any action yet but agreed to complete within the given timeline.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	১১-০৮-২০১৭
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	<p>Previous Timeline: N/A, during CAP (CAP-01) explanation factory claimed completed. Final Timeline: 08/11/2017. Not taken any action regarding this issue but factory agreed to complete the issue within the timeline. 09/03/2020: As built drawing has been submitted as a part of DEA to DIFE for approval. 02/09/2020: Same as last inspection. 08/12/2020: As built drawing is a part of DEA. DEA has been submitted to DIFE on 04.07.19 for approval but not found any taskforce meeting for this factory yet. 09/06/2021: This issue covers under DEA. The factory management have submitted all structural design &amp; drawings by an enlisted firm of DIFE to DIFE RCC on 04/07/2019. A notification meeting held on RCC office regarding this issue in presence of the factory management &amp; consulting firm personnel on 23/07/2020. They were told to re-submit these design &amp; drawings with some reviews to DIFE RCC within 11/10/2020. But those are not submitted yet. Now the factory management is instructed to submit these design &amp; drawings with proper corrections by their consulting firm to DIFE RCC within 10/07/2021. 23.08.2021: Correction Design drawing not submitted yet. Now the factory management is instructed to submit these design &amp; drawings with proper corrections by their consulting firm to DIFE RCC 16/08/2022: DEA report must be resubmitted to DIFE for approval as soon as possible. 02/04/2023: DEA report should be resubmitted to DIFE for approval as soon as possible.</p>

### সংযুক্তিসমূহ ( ৪ )

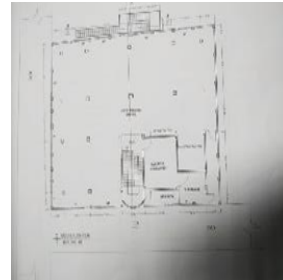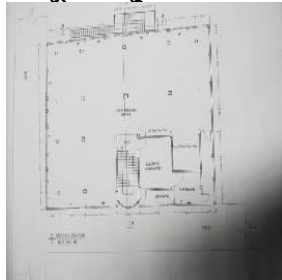


৩. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Core test
ক্যাপ আইটেম ক্যাটাগরি	

৩.১. কার্যক্রম

কার্যক্রম	Coring with 4 nos. 4in cores ( 3 in when taken from column ) for each of the building & scanning of rebars at ground floor
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not been taken any action yet but agreed to complete within the given timeline.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	১১-০৮-২০১৭
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	<p>Previous Timeline: N/A, during CAP ( CAP-01 ) explanation factory claimed completed. Final Timeline: 08/11/2017. Not taken any action regarding this issue but factory agreed to complete the issue within the timeline. 09/03/2020: Core test has been done as a part of DEA. 02/09/2020: Progress status same as last inspection. 08/12/2020: Core test has been completed as a part of DEA. 17/02/2021: same as previous. 09/06/2021: This issue covers under DEA. The factory management have submitted all structural design &amp; drawings by an enlisted firm of DIFE to DIFE RCC on 04/07/2019. A notification meeting held on RCC office regarding this issue in presence of the factory management &amp; consulting firm personnel on 23/07/2020. They were told to re-submit these design &amp; drawings with some reviews to DIFE RCC within 11/10/2020. But those are not submitted yet. Now the factory management is instructed to submit these design &amp; drawings with proper corrections by their consulting firm to DIFE RCC within 10/07/2021. 23.08.2021: This issue covers under DEA. The factory management have submitted all structural design &amp; drawings by an enlisted firm of DIFE to DIFE RCC on 04/07/2019. 16/08/2022: DEA report must be resubmitted to DIFE for approval as soon as possible. Core Test report was found during inspection date. 02/04/2023: This issue covers under DEA. DEA report should be resubmitted to DIFE for approval as soon as possible. Core Test report was found during inspection date.</p>

সংযুক্তিসমূহ ( ৪ )

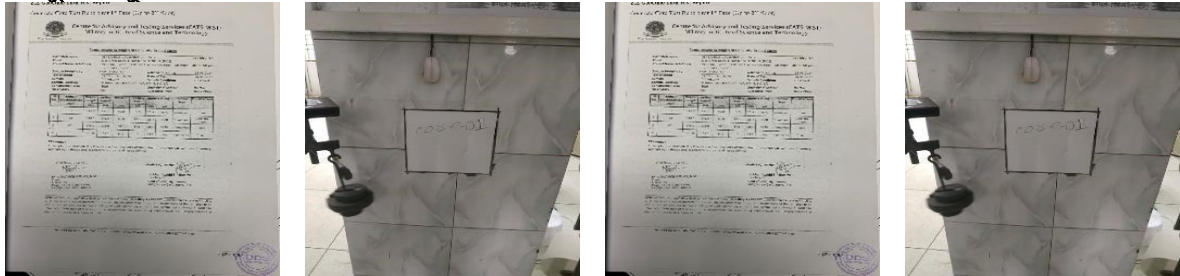

৪. পর্যবেক্ষণ

পরিদর্শন পর্ববেষ্টিত	Adequacy
কাপ আইটেম ক্যাটাগরি	

#### ৪.১. কার্যক্রম

কার্যক্রম	A structural adequacy of the building will be needed to further vertical extention .
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We have not been taken any action yet but agreed to complete within the given timeline.
অগ্রাধিকার	৬ মাস
চূড়ান্ত সময়সীমা	১১-০৮-২০১৭
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	<p>Previous Timeline: N/A, during CAP (CAP-01) explanation factory claimed completed. Final Timeline: 08/11/2017. Not taken any action regarding this issue but factory agreed to complete the issue within the timeline. 09/03/2020: Structural adequacy has been completed as a part of DEA. 02/09/2020: Same as last inspection. 08/12/2020: Structural adequacy is a part of DEA. DEA has been submitted to DIFE on 04.07.19 for approval but not found any taskforce meeting for this factory yet. 17/02/2021: A notification meeting held on September 23, 2020 and some review was found But review item is not submitted yet.</p> <p>09/06/2021: This issue covers under DEA. The factory management have submitted all structural design &amp; drawings by an enlisted firm of DIFE to DIFE RCC on 04/07/2019. A notification meeting held on RCC office regarding this issue in presence of the factory management &amp; consulting firm personnel on 23/07/2020. They were told to re-submit these design &amp; drawings with some reviews to DIFE RCC within 11/10/2020. But those are not submitted yet. Now the factory management is instructed to submit these design &amp; drawings with proper corrections by their consulting firm to DIFE RCC within 10/07/2021. 23.08.2021: This issue covers under DEA. Correction Design drawing not submitted yet. Now the factory management is instructed to submit these design &amp; drawings with proper corrections by their consulting firm to DIFE RCC . 16/08/2022: DEA report must be resubmitted to DIFE for approval as soon as possible. 02/04/2023: DEA report should be resubmitted to DIFE for approval as soon as possible.</p>
