



গণপ্রজাতন্ত্রী বাংলাদেশ সরকার
শ্রম ও কর্মসংস্থান মন্ত্রণালয়
কলকারখানা ও প্রতিষ্ঠান পরিদর্শন অধিদপ্তর

"সুস্থ শ্রমিক, শোভন কর্মপরিবেশ;
গড়ে তুলবে স্মার্ট বাংলাদেশ"

ক্যাপ পর্যবেক্ষণের তথ্য


কারখানার নাম	ইউমে লিটিং (বিডি) লিমিটেড
ঠিকানা	Charkidirpur, Pashchim gumdondhi, Boalkhali, Chattogram
কারখানার কোড	CHT191
কালার কোড	
মূল্যায়নের ধরণ: কাঠামোগত মূল্যায়ন	পর্যবেক্ষণের তারিখ: ২৩-০২-২০২৩
১. পর্যবেক্ষণ	

পরিদর্শন পর্যবেক্ষণ	Approval Drawings
কাপ আইটেম ক্যাটাগরি	

১.১. কার্যক্রম

কার্যক্রম	As-built architectural and structural drawings of the building to be prepared and submitted for approval by appropriate authority. As part of this process the building engineer will be required to make a number of checks on the inconsistencies between the structural design and the as-built construction.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We will engage a building engineer to prepare as-built architectural and structural drawings for the building and will submit for approval by appropriate authority and as part of this process the building engineer will make a number of checks on the as-built construction.
অগ্রাধিকার	প্রযোজ্য নয়
চূড়ান্ত সময়সীমা	২০-১০-২০১৭
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	On 19/12/2018: Waiting for DEA approval On 26/02/2019: Same as before On 01/10/2020: DEA Approved. On 06/01/2021: Design Drawing and DEA Approved. 01.09.2021: This issue is solved. 24-05-2022 (CCV): Few mismatch in as-built Structural drawing have been found in column and beam sizes. As-built drawing and DEA report must be updated and submitted to DIFE. 23-02-2023 (CCVV): During the day of CCV, it was found that factory have corrected all the necessary items related to as-built documents & approval documents have been found during the day of visit.

সংযুক্তিসমূহ (২)

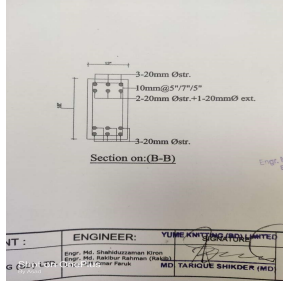

২. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Non-Engineered Stair
কাপ আইটেম ক্যাটাগরি	

২.১. কার্যক্রম

কার্যক্রম	The connection of steel stair needs to be checked by building engineer and the bracing system is required to ensure the stability of the structure. Carry out any remedial actions as directed by the Building Engineer for steel stairs.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	We will engage a building engineer to check the connection of steel stair and bracing system to ensure the stability of the structure. We will carry out any remedial actions as directed by the Building Engineer for steel stairs.
অগ্রাধিকার	প্রয়োজ্য নয়
চূড়ান্ত সময়সীমা	২০-১০-২০১৭
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	On 30/10/2018: Submitted with DEA. After approval they will carry out the remedial work (if Any) On 19/12/2018: Same as before On 26/02/2019: Same as before On 06/01/2021: Still not started Retrofitting work of Steel Stair. 01.09.2021: Still not start retrofitting work. 24-05-2022 (CCVV): Factory did not started retrofitting work of Steel Stair. 23-02-2023 (CCVV): Retrofitting of stair have been done. The Issue have been resolved.

সংযুক্তিসমূহ (২)

