



গণপ্রজাতন্ত্রী বাংলাদেশ সরকার
শ্রম ও কর্মসংস্থান মন্ত্রণালয়
কলকারখানা ও প্রতিষ্ঠান পরিদর্শন অধিদপ্তর

"শ্রমজীবী মানুষের অধিকার,
বৈষম্যহীন বাংলাদেশের অঙ্গীকার"

ক্যাপ পর্যবেক্ষণের তথ্য

কারখানার নাম	শোনন সোয়েটারস লিঃ
ঠিকানা	Plot-A-118. S-36, BSCIC, Konabari, Gazipur
কারখানার কোড	GZP309
কালার কোড	
মূল্যায়নের ধরণ: কঠামোগত মূল্যায়ন	পর্যবেক্ষণের তারিখ: ১২-০৪-২০২৩
১. পর্যবেক্ষণ	

পরিদর্শন পর্যবেক্ষণ	Moderated Stressed Column
কাপ আইটেম কাটাগরি	

১.১. কার্যক্রম

কার্যক্রম	Factory Engineer to review design, loads and columns stresses in area identified above B6 column.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	
অগ্রাধিকার	প্রযোজ্য নয়
চূড়ান্ত সময়সীমা	—
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	<p>09-April-2019: DEA reports and submission letter to DIFE have been found on site. Approval of DEA report is In progress. 07-Nov-2019: DEA report has been found at site. Received copy of submission of DEA report to DIFE has been found. 04-Mar-2020: DEA report has been received by DIFE dated on 10.12.2018. But, some mismatch are found in DEA documents and as built drawings. Evidence of ferro scan and column strip cutting were missing in DEA report. Toilet build up level are not match with as built drawing. Some build up observed in wash section but missing in drawing. Layout and capacity of plastic water tank mentioned in as built drawing are not match with as built condition. 19.10.2020: DEA report and design drawing submitted to DIFE for approval and the letter was found onsite.</p> <p>06.01.2021: DEA report has been found at site. Received copy of submission of DEA report to DIFE has been found. 10.08.2021: DEA report has been found at site. Received copy of submission of DEA report to DIFE has been found. 17.08.2022: DEA report has been found at site but not updated. Factory have some correction. After complete all correction they submit updated DEA document to DIFE as son as possible. 12-04-2023: Same as previous visit.</p>

সংযুক্তিসমূহ (৪)



পরিদর্শন পর্যবেক্ষণ	Moderated Stressed Column
ক্যাপ আইটেম ক্যাটাগরি	

২.১. কার্যক্রম

কার্যক্রম	Verify in-situ concrete stresses either by 100mm dia. cores or existing cylinder strength data for identified B6 columns.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	
অগ্রাধিকার	প্রযোজ্য নয়
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	সংশোধিত
মন্তব্য	09-April-2019: Core test results have been found on site with different name of the factory. No evidence of core cutting have been observed on site. 07-Nov-2019: Core test results have been found on site with different name of the factory. No evidence of core cutting has been observed on site. 04-Mar-2020: Core test report was found but factory name mentioned in core test report is not matched. Also, evidence of core cutting was not possible to verify due to plastering work. 19.10.2020: DEA report was submitted to DIFE for approval which covers the core test report. But the core test report states different factory name and no core cutting evidence was seen during inspection. 06-01-2021: Core test results have been found on site with different name of the factory. No evidence of core cutting have been observed on site. 10.08.2021: Core test results have been found on site with different name of the factory. No evidence of core cutting have been observed on site. 17.08.2022: Core test results have been found on site with different name of the factory. factory management says that, when the DEA work start & Core has been taken of the building then the factory name is Mega Fashion Wear Ltd. DEA Completion, return for correction & resubmission continue after a long time. in the mean time factory name is change by Shanon Sweater Ltd. Again after a same day factory change name by Swan Sweater Ltd. Also we verify core layout plan. core layout plan are matched with provide core layout plan. 12.04.2023: Completed.

সংযুক্তিসমূহ (৮)




৩. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Moderated Stressed Column
কাপ আইটেম ক্যাটাগরি	

৩.১. কার্যক্রম

কার্যক্রম	Produce and actively manage a loading plan for all floor plates within the factory giving consideration to floor capacity and column capacity.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	
অগ্রাধিকার	প্রযোজ্য নয়
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	09-April-2019: Load plan has been found without approval and not posted. 07-Nov-2019: No load marking has been observed at site. Load plan without seal and signature has been found at site. 04-Mar-2020: Load plan has been found posted but not approved yet. Also, no load marking has been observed at site. 19.10.2020: Load plan was found but not approved. They submitted load plan for approval. Load marking was not given on each floors.at site. 06.01.2021: Load plan was found but not approved. They submitted load plan for approval. Load marking was not given on each floors. 10.08.2021: Load plan was found but not approved. They submitted load plan for approval. Load marking was not given on each floors. 17.08.2022: Factory has been submit DEA report to DIFE but not approved yet. so approved floor load plan not found during visit day. Load marking not found some area. 12.04.2023: Same as previous.

সংযুক্তিসমূহ (৪)

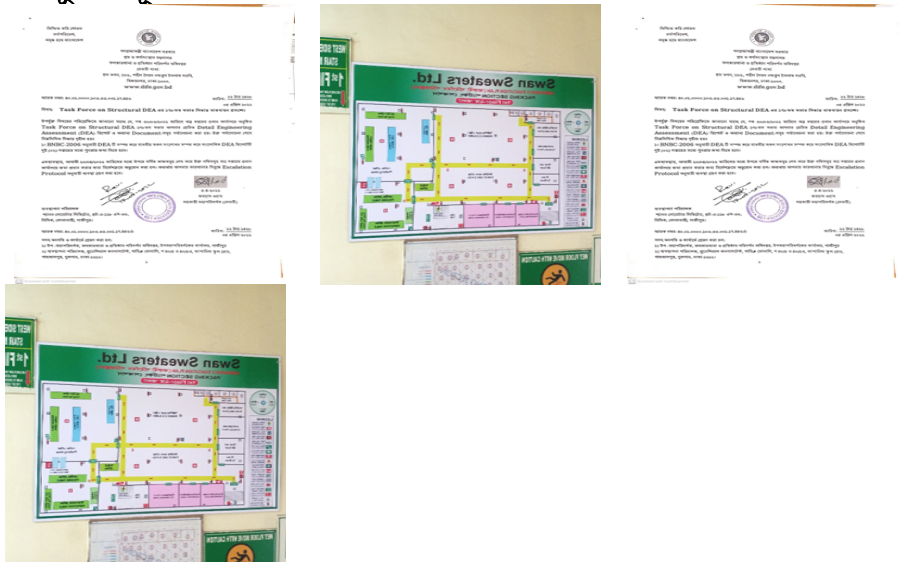

৪. পর্যবেক্ষণ

পরিদর্শন পর্যবেক্ষণ	Lateral Stability System
কাপ আইটেম কাটাগরি	

৪.১. কার্যক্রম

কার্যক্রম	Building Engineer needs to check existing flat slab system. Lateral system is required to ensure stability of the structure.
সুপারিশের তথ্যসূত্র	
কারখানার কার্যক্রম	
অগ্রাধিকার	প্রযোজ্য নয়
চূড়ান্ত সময়সীমা	-
সংশোধিত সময়সীমা	০১-০১-১৯৭০
অগ্রগতির অবস্থা	চলমান
মন্তব্য	09-April-2019: DEA reports and submission letter to DIFE have been found on site. Approval of DEA report is In progress. 07-Nov-2019: DEA report has been found at site. Received copy of submission of DEA report to DIFE has been found. 04-Mar-2020: This issue is covered in DEA. DEA report has been received by DIFE dated on 10.12.2018. 19.10.2020: DEA report was submitted on 2018 received by DIFE for approval. 06-01-2021: DEA report has been found at site. Received copy of submission of DEA report to DIFE has been found. 10.08.2021: DEA report has been found at site. Received copy of submission of DEA report to DIFE has been found. 17.08.2022: DEA report has been found at site but not updated. Factory have some correction. After complete all correction they submit updated DEA document to DIFE as son as possible. 12.04.2023: Same as previous.

সংযুক্তিসমূহ (৪)

